

Albuquerque Environmental Management Critical Closure Path

Exhibit E-6

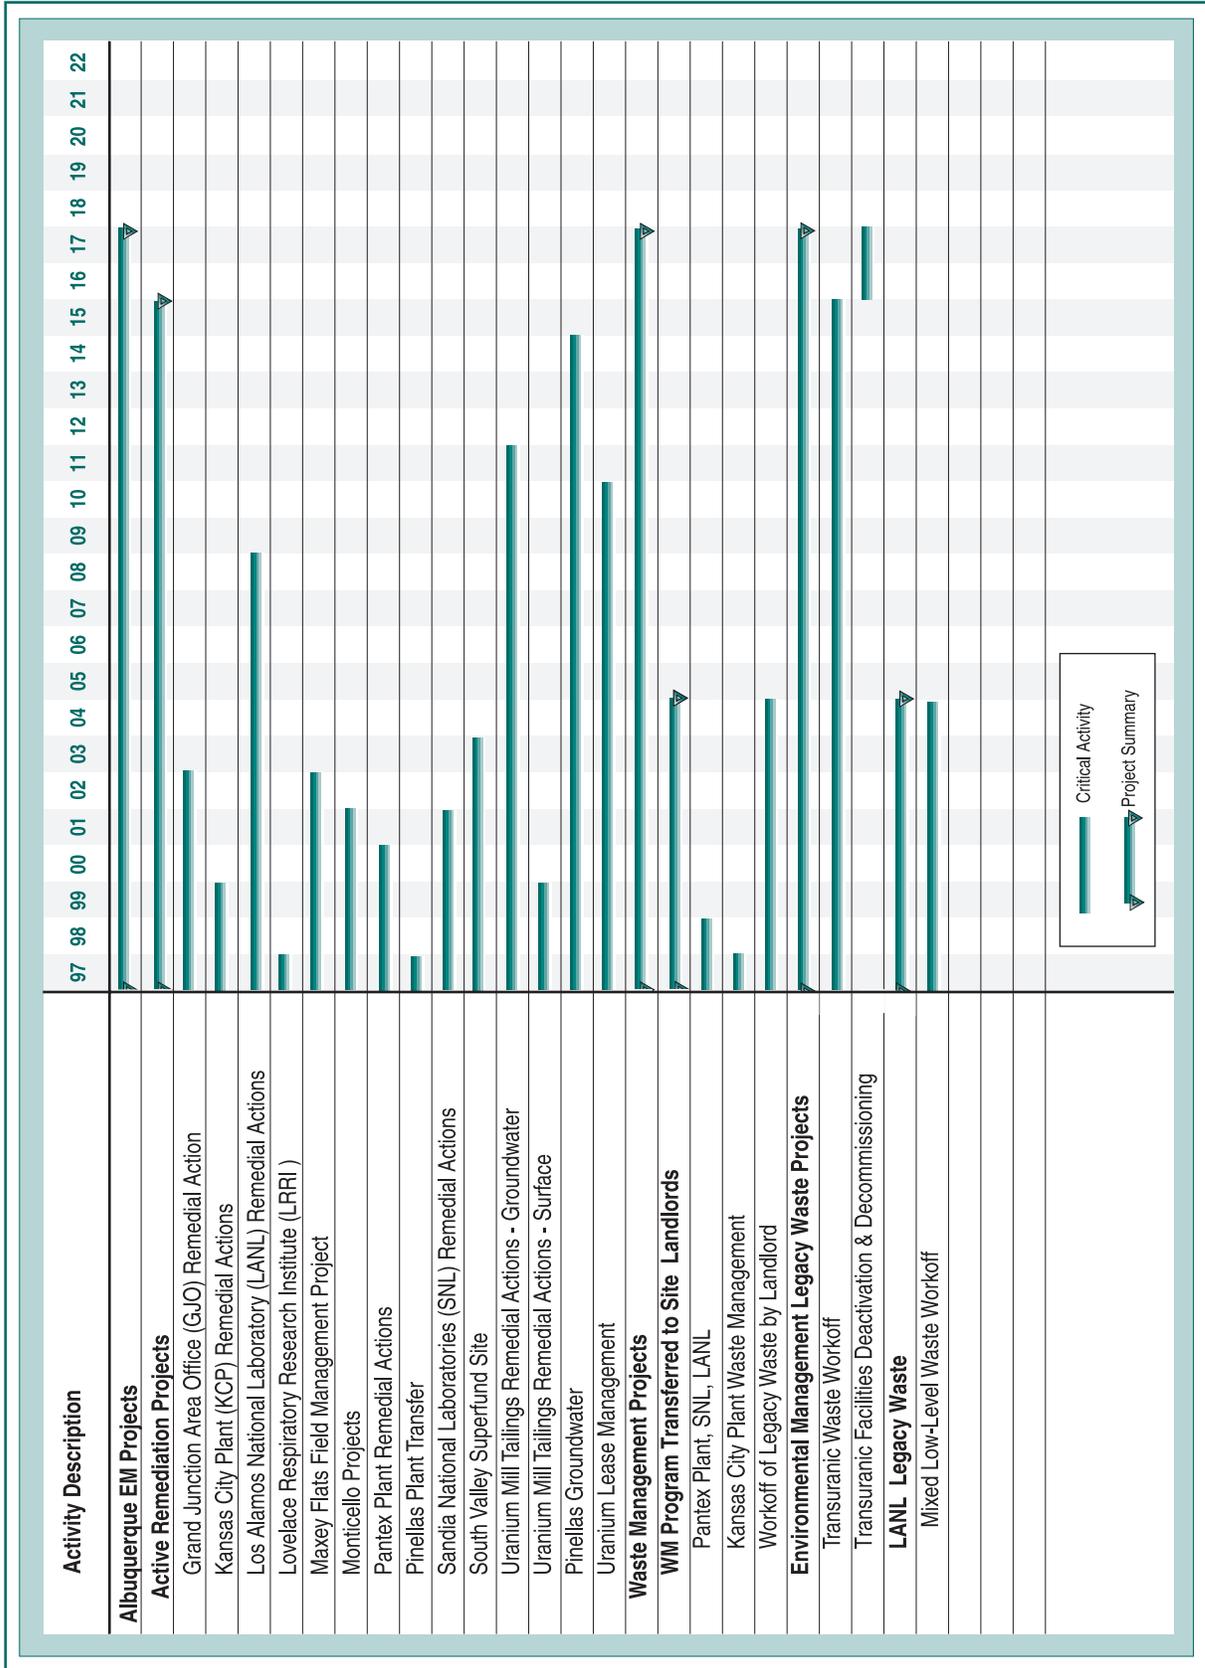


Exhibit E-7
Summary of High Programmatic Risk Activities/Milestones:
Albuquerque Operations Office

Site	Project, Activity, Event	Start/End Dates	Programmatic Risk Categories		
			Technological	Work Scope Definition	Intersite Dependency
GJO	Supplemental limits must be approved on Bldg. 7	Oct 99/ Oct 00	1	5	1
	Supplemental limits must be approved on Bldg. 20	Oct 99/ Oct 00	1	5	1
	Buried utilities must be investigated and any contamination found must be minimal	Oct 01/ Sep 02	1	5	3
KCP	Complete 95th Terrace Assessment	Jan 98/ Jun 99	1	4	1
SNL	WIPP opens in May 1998	May 98	1	4	4
	Operation of Auxiliary Hot Cell Facility for packaging of remote-handled TRU	Oct 97/ Sep 99	1	4	4
	Develop system to ship remote-handled TRU to WIPP or Los Alamos National Laboratory	Oct 99/ Sep 00	2	4	5
	Complete mixed waste treatment per Site Treatment Plan (except for mixed TRU waste)	Oct 97/ Sep 02	4	4	5
	Work off of historical MW	Oct 97/ Sep 06	3	4	5
South Valley	Long-term buyout	Apr 03/ Sep 03	1	4	1
UMTRA	Maybell site construction completion	Sep 98	3	4	5
	Maybell site certification license and transfer to GJO for long-term surveillance and monitoring	Sep 99	5	5	5
