


Exhibit E-42 Oakland Operations Office Critical Closure Path

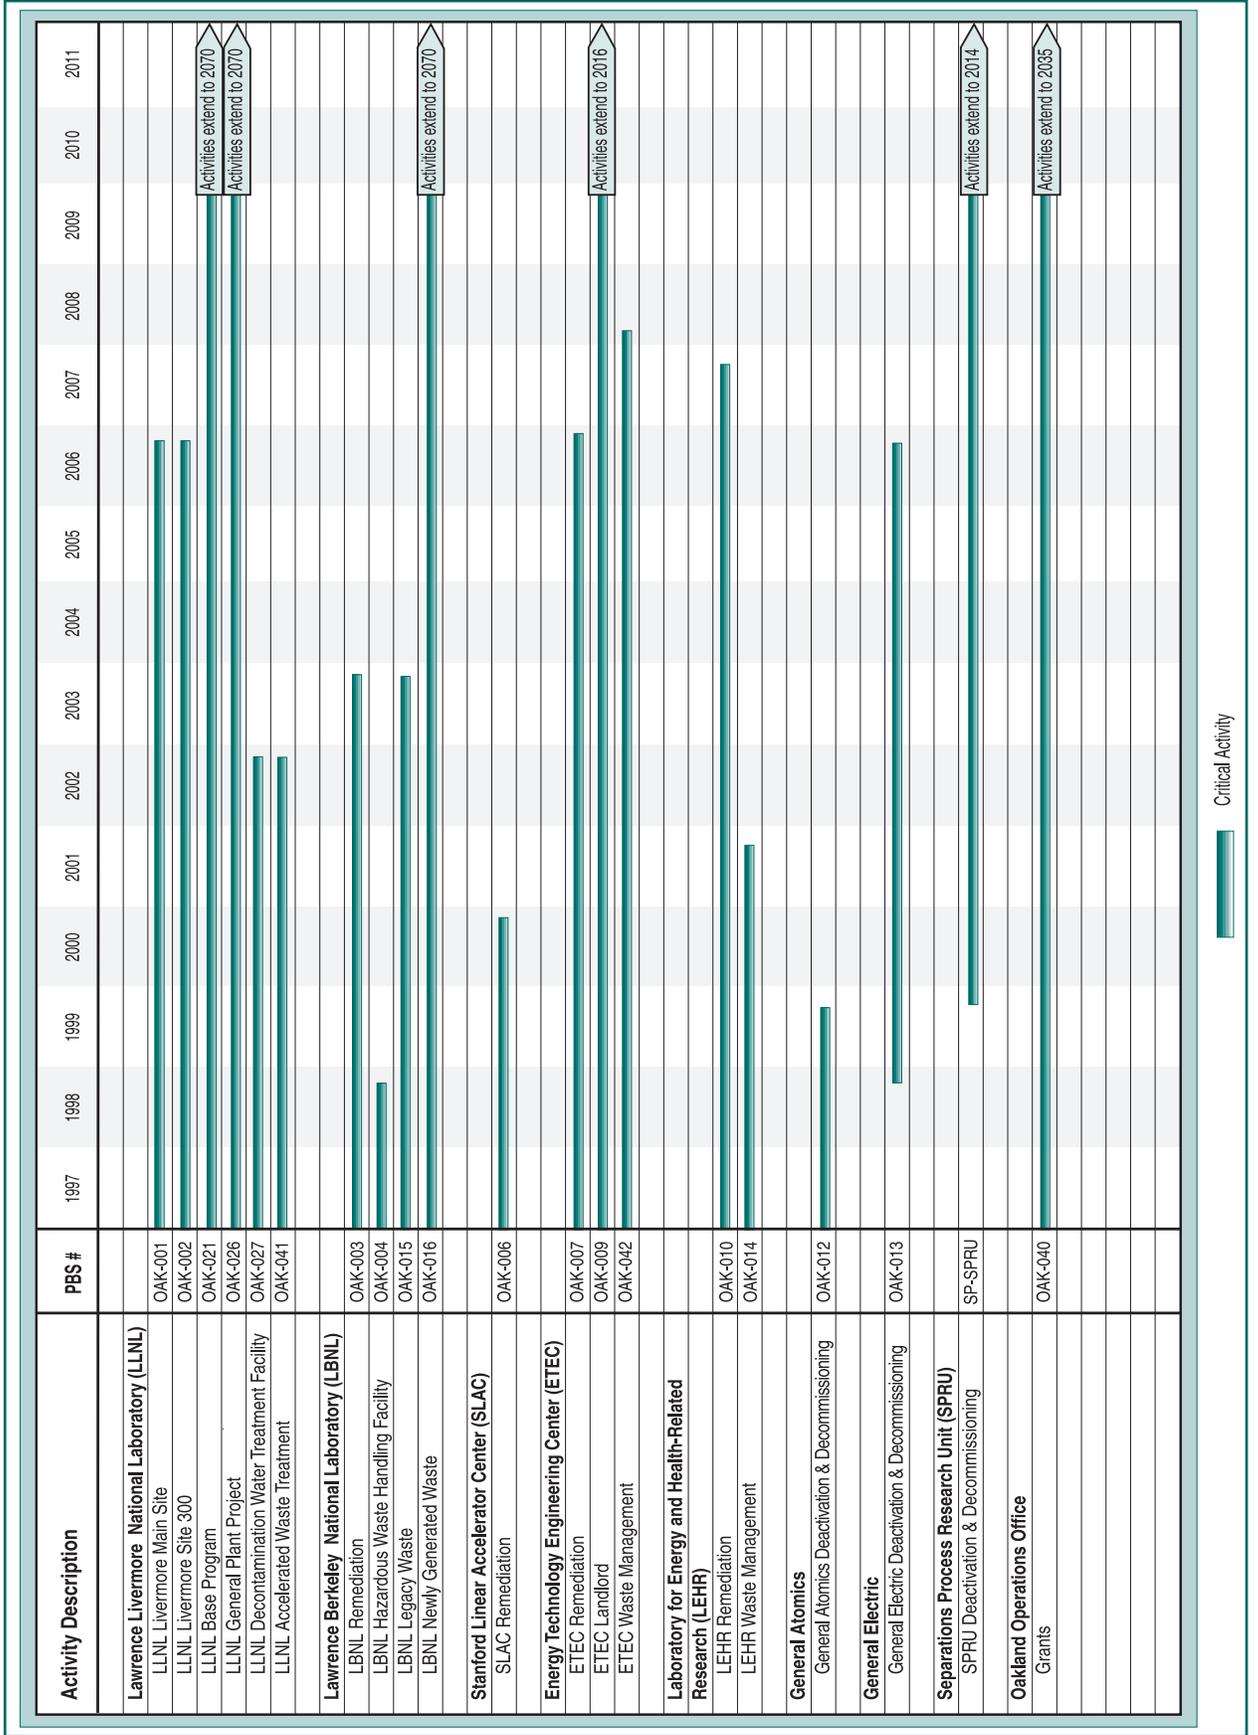

Critical Activity

Completion of the EM mission at the Oakland Operations Office as scheduled will depend on the timely accomplishment of critical activities. Appendix D provides a complete definition of programmatic risk. Exhibit E-43 presents a summary of activities/milestones on the critical closure path that have high programmatic risk (programmatic risk scores of 4 or 5 in any category). The Oakland Operations Office version of *Paths to Closure* provides more details on the management approach for these high programmatic risk issues.

Exhibit E-43
Summary of High Programmatic Risk Activities/Milestones:
Oakland Operations Office

Site	Project, Activity, Event	Start/End Dates	Programmatic Risk Categories		
			Technological	Work Scope Definition	Intersite Dependency
GA	Package and ship irradiated fuel materials to INEEL for interim storage	Jun 95/ Mar 00	1	4	4
LBNL	Complete characterization and certification for off site disposal of all LBNL legacy waste.	Oct 95/ Sep 70	1	4	3
	Completion of Western Dog Pens Area Removal Action	Apr 00/ Sep 00	2	3	4
LEHR	Completion of disposal of mixed low-level waste/material	May 01/ Aug 01	2	3	4
	No Action ROD for DOE Areas	Sep 01/ Jun 02	NA	4	3
